


Residential Sound Insulation Program Flow Chart & Property Progress 12 Month Tracker

Time Period: March 2013 through March 2014

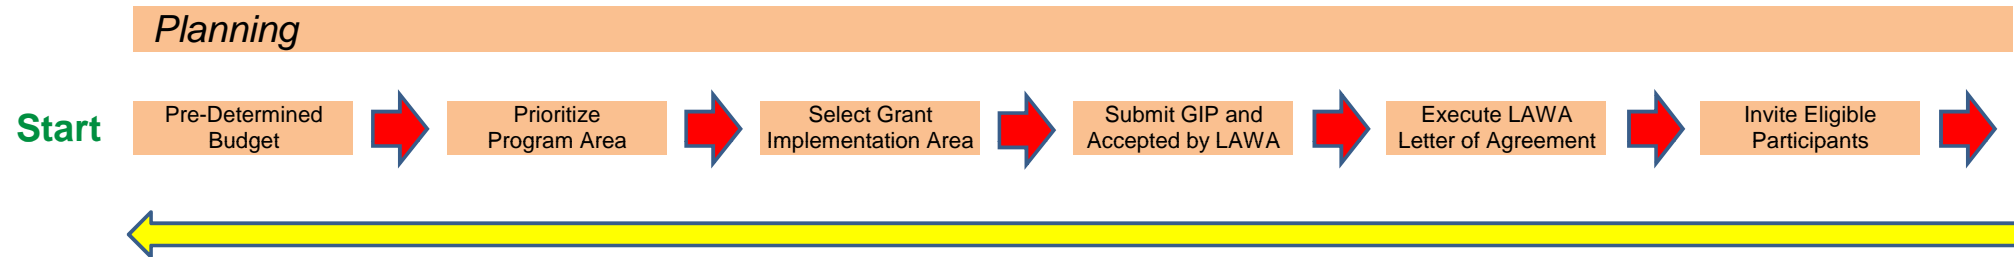

Mayor Negotiates MOU with LAWA

Mayor and Executive Director of Los Angeles World Airports (LAWA) sign Memorandum of Understanding (MOU) for improved program performance by City's Residential Sound Insulation Program

812 Units
Letters sent to Property Owners
within the Noise Contours

Design



356 Units
Letters Returned from interested Property Owners



222 Units
Properties without preliminary Building & Safety Code Violations




384 Units
Properties evaluated and grouped to be assigned to architecture and engineering (A&E) firms



99 Units
Currently being designed by architectural and engineering firms

705 Units

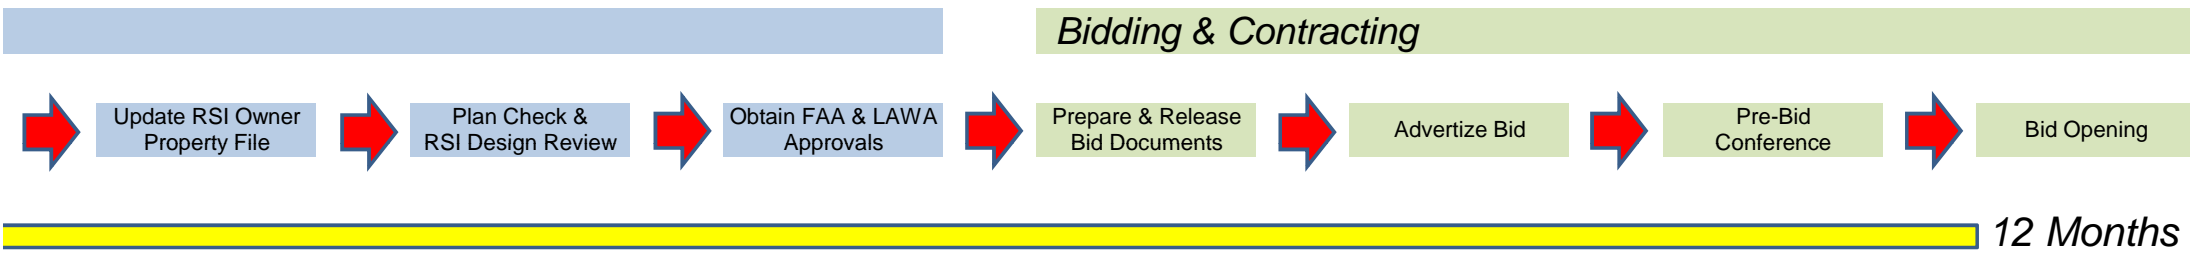

533 Units
Currently being put "on the street" for contractor bids

Pre-Construction: 2 to 3 months



234 Units

Mayor and City Council have approved and contracts are being signed



92 Units

Home-specific windows, doors, sound insulation materials, and heating and air conditioning units are being ordered

Construction: 3 to 6 months

Post-Construction: 2 to 4 weeks


Active Construction



Final Submittals
Warranties, etc.



Final Payments



49 Units

Currently under construction with placement of windows, doors, sound insulation materials, and heating and air conditioning units

1,157 Units

Close-Out

Post-Modification
Noise Survey



Administrative
Review (Compliance)

Submit Final
Architect's Report

Issue Notice of
Compliance

Submit Project Report &
Certification of Completion

Finished



249 Units

Currently in "close-out" and each group of units will be brought to the Mayor and City Council for final project acceptance and close-out
